



ACH Group LLC DBA BasementRemodeling.com
HOME IMPROVEMENT SERVICES CONTRACT

THIS HOME IMPROVEMENT SERVICES CONTRACT (the “Agreement” or “Contract”) is entered into as of the date provided below (the “Date of Transaction”) with the Parties’ signatures by and between:

(1) **ACH GROUP LLC DBA BASEMENTREMODELING.COM** (the “Contractor”), MD License: 129172, DC License: 410516000631, VA License: 2705159425, located at 5300 Kilmer Pl., Hyattsville, Maryland 20781, Phone: (877) 224-2434, Fax: (877) 224-3661 and (2) John Ring (the “Owner”).

Owner Address: 5801 Searl Ter, Bethesda, MD 20816
Cell Phone Number: (603)-996-1707 Email Address: rayjohnring@gmail.com

Date this Agreement was signed by Owner: 3/31/2026

Job Site Address: 5801 Searl Ter, Bethesda, MD 20816

I. CONTRACT PRICE & PAYMENT TERMS.

A. Contract Price. In exchange for the Services described herein and in Section II (Description of the Included Services), Owner agrees to pay Contractor the total contract price of:


\$ 102,293.00, payable in installments electronically (the “Services Fee”). The Contract Price may reflect discounts, incentives, or promotional pricing applied to the aggregate value of the line items set forth in the Proposal.

Invoices will be sent to Owner via email. Each email will include a PDF copy of the invoice and a secure link to submit payment on-line. Please refer to the following page for instructions. Email address for invoice delivery: rayjohnring@gmail.com

Contractor does not accept credit card payments unless previously agreed to in writing by the Parties. If credit card payment is approved, any applicable cash or check discount shall be waived, and a processing fee of three percent (3%) will be added to the payment amount.

B. Payment Schedule:

1. **DEPOSIT OF \$1,000.** The Deposit shall be applied toward the Contract Price. In the event of cancellation by Owner, Contractor shall be entitled to retain the Deposit to cover administrative costs, scheduling, design, pre-construction services, and other costs incurred prior to cancellation. Any remaining balance, if applicable, shall be handled in accordance with applicable law.
2. **PAYMENT 1 of \$ 10,229.30**, due upon signing this agreement. Ten Percent (10%) of Services Fee. If Owner cancels the Project prior to the Official Start Date (as defined in Section III), Contractor shall be entitled to retain a minimum of 50% to cover actual costs incurred, including administrative, permit preparation, design, and scheduling costs. Any remaining balance shall be refunded in accordance with applicable law.

ACCEPTED BY: 
A1EFF9FF7DCB4C2...

3. **PAYMENT 2 of \$ 15,343.95**, due upon commencement of work. Fifteen Percent (15%) of Services Fee.
4. **PAYMENT 3 of \$ 25,573.25**, when job is 35% completed. Twenty-Five (25%) Percent of Services Fee. WHEN FRAMING, ROUGH-IN ELECTRICAL, PLUMBING (if any), AND HVAC (if any) IS COMPLETED.
5. **PAYMENT 4 of \$ 25,573.25**, when job is 70% completed. Twenty-Five (25%) of Services Fee.
6. **PAYMENT 5 of \$ 24,573.25**, when job is 100% completed. Twenty-Five (25%) of Services Fee minus the Deposit of \$1,000.



AFTER THE AGREEMENT IS SIGNED OWNER WILL RECEIVE AN EMAIL WITH "PAYMENT 1" INVOICE. SEE THE INSTRUCTIONS ON HOW TO PAY INVOICES ONLINE ON THE SCREENSHOT BELOW.

HOW TO PAY AN INVOICE ONLINE SCREENSHOT TUTORIAL:

ACH Group LLC dba Basement Masters  Inbox - MAIN ACH 6:19 PM 

Invoice 20190401-02 from ACH Group LLC dba Basement Masters
To: [REDACTED]
Reply-To: Basement Masters Billing Department

Pay this button to review and pay the invoice

PDF Version of the invoice

Click this button to Review and pay the invoice

ACH Group LLC dba Basement Masters

Dear [REDACTED],

Here's your invoice! We appreciate your prompt payment.

Thanks for your business!
ACH Group LLC dba Basement Masters

INVOICE 20190401-02

DUE 04/01/2019

\$1.00

Review and pay

Powered by QuickBooks

ACH Group LLC dba Basement Masters
1680 E Gude dr, STE 100 Rockville, MD 20850
(301) 653-0885 billing@basementmasters.com

If you receive an email that seems fraudulent, please check with the business owner before paying.



© Intuit, Inc. All rights reserved. [Privacy](#) | [Security](#) | [Terms of Service](#)

ACH Group LLC dba Basement Masters
1680 E Gude dr, STE 100
Rockville, MD 20850
(301) 653-0885





II. DESCRIPTION OF THE INCLUDED SERVICES.

- A. For a price indicated in Clause I of this Agreement, Contractor agrees to complete the Services, as identified in the attached "Proposal" which provides a full detailed description of the Services. The Proposal is hereby incorporated by reference into this Agreement.
- B. The Parties agree that Contractor shall be responsible for securing all necessary permits (if specified in Proposal) and scheduling all necessary inspections (if needed) for the Project.
- C. Contractor will only be responsible to provide the Services outlined in Proposal. Contractor shall not be responsible for any interpretation of the project scope beyond what is expressly stated in the Proposal. The only scope of work included is the scope outlined in the Proposal. Please read each item in Proposal. If it is not expressly noted and described in Proposal, it is NOT part of the contract, and NOT included.
- D. If Owner requests removal or credit for any item included in the Proposal, and the Contract Price reflects any discount, incentive, or price reduction from the aggregate value of the line items set forth in the Proposal, any credit issued shall reflect the same proportional reduction applied to the Contract Price. Specifically, the credit amount shall be calculated by applying the same percentage reduction originally applied to the total Contract Price to the value of the removed item.

III. COMMENCEMENT OF SERVICES.

- A. **Preliminary Start Date:** 04/28/2026. The "Preliminary Start Date" is the date mutually agreed upon by Contractor and Owner for the Pre-Construction Meeting (or Pre-Demolition Meeting, if demolition is included in the scope of work). The Preliminary Start Date may be adjusted due to circumstances beyond Contractor's reasonable control, including but not limited to weather conditions, permit issuance delays, Owner's availability, other unforeseen conditions. Adjustment of the Preliminary Start Date shall not constitute a breach of this Agreement.
- B. Project Start Date or the "Official Start Date" shall be the date on which Contractor conducts the scheduled Pre-Construction Meeting with Owner. If demolition is included as part of the Project scope, the "Official Start Date" shall instead be the date on which Contractor conducts the Pre-Demolition Meeting with Owner.
- C. Commencement of Work. The Project shall be deemed commenced upon the Official Start Date, regardless of whether physical construction activities begin on that same date.

IV. APPROXIMATE COMPLETION DATE.

- A. Services under this Agreement will be Substantially Complete on or before twelve (12) weeks after Official Start Date unless stated otherwise.
- B. Delays resulting from events beyond Contractor's control, including but not limited to delays stemming from the procurement of Owner selected special order items, delays arising from the provision of additional services at the request of Owner, and delays attributable to extended inspection wait times, have the capacity to substantially extend the projected completion date.

V. COMPLIANCE WITH LAW.

- A. Contractor and Owner mutually commit to use reasonable care to meet any and all legal requirements of state, federal and/or local Law when discharging their responsibilities under this Agreement.

VI. OWNER'S RESPONSIBILITIES.

- A. Owner shall have sole responsibility to secure financing for the Services and shall pay any and all fees, charges, and/or other costs of such financing, including, but not limited to, inspection fees charged by any lender. The non-performance of any lender shall not affect any obligations of Owner to Contractor hereunder. Owner hereby authorizes and directs any lender on the Project to furnish Contractor with full information on any undisbursed loan proceeds when requested by Contractor.
- B. Owner shall not interfere with or permit others to interfere with, stop, hinder, or delay completion of the Project by Contractor or Subcontractors except as provided under this Agreement.

VII. REPRESENTATIONS BY OWNER.

- A. Owner has reported to Contractor all conditions known to Owner which may not be apparent to Contractor, and which might significantly increase cost of the Project and/or delay completion of the Project. These concealed conditions include, but are not limited to, any and all hazards on the Job Site, unsuitable soil conditions, prior defective work of others, any latent defects in the plans and/or specifications, earlier attempts to do similar and/or related work, and any obligations imposed by government.



- B. Contractor may hire or engage one (1) or more subcontractors to perform any or all of its obligations under this Agreement; provided, that (i) Contractor shall use the same degree of care in selecting any such subcontractor as it would if such contractor was being retained to provide similar services to Contractor and (ii) Contractor shall in all cases remain responsible for all of its obligations under this Agreement with respect to the scope of the Services, the standard for such Services and the content of the Services provided to Owner.

VIII. DISCLAIMER BY OWNER, RELIANCE BY CONTRACTOR.

- A. Owner has provided to Contractor any and all relevant information on subsurface and/or concealed conditions at the Job Site. Except to the extent that Contractor knows this information to be false, Contractor is entitled to rely on the accuracy of any information provided by Owner to Contractor.

IX. LIENS & WAIVERS.

- A. Anyone who helps improve Owner's property, but who is not paid, may record what is called a mechanics' lien on Owner's property. A mechanics' lien is a claim, like a mortgage or home equity loan, made against Owner's property and recorded with the county recorder. Contractor reserves all rights to file and enforce a mechanics' lien in accordance with applicable law in the event of nonpayment.

X. FINAL INSPECTIONS & LIENS.

- A. Upon notification by Contractor of substantial completion of Project, Owner and Contractor will inspect the work performed, and at that time, Owner will prepare a punch list that identifies any incomplete work and/or deficiencies in workmanship or materials. Owner may withhold only a reasonable amount directly attributable to the incomplete punch list items, not to exceed the estimated cost of correcting such items. Completion of the punch list items shall be made within seven (7) days from the date of the punch list preparation, subject to material availability and inspection scheduling. When the punch list items are completed, Owner will pay Contractor the balance of the Agreement price within two (2) days of request. At that time, Contractor will deliver to Owner a release of all liens/written agreement that all required payments have been made. Failure to timely pay shall constitute a material breach.

XI. CHANGE ORDERS.

- A. Both Contractor and Owner must agree to all change orders. Change orders may be documented in writing or via email communication between the Parties. Owner acknowledges and agrees that full payment of the total amount stated in a change order constitutes acceptance and authorization of the additional or modified work described therein. Contractor shall not be obligated to commence any additional or modified work until full payment of the change order amount has been received. No verbal change order shall be valid or enforceable.

Email confirmation and full payment of the change order amount shall constitute a binding modification to this Agreement without the need for additional signatures.

XII. INSURANCE & RISK OF LOSS.

- A. Contractor agrees to maintain workers' compensation insurance and/or waiver and liability insurance to protect the Owner from liability claims for damages because of bodily injury, including death, and from liability for damages to the Owner's property. Certificates of insurance shall be provided upon reasonable request.

XIII. LIABILITY & INDEMNIFICATION.

- A. To the fullest extent permitted by law, Contractor shall indemnify, defend, and hold harmless Owner from and against claims, damages, losses, and expenses, including reasonable attorneys' fees, arising out of or resulting from bodily injury, sickness, disease, or death, or damage to property, but only to the extent caused by the negligent acts or omissions of Contractor, its employees, subcontractors, or agents in the performance of the Services.
- B. This obligation shall not apply to the extent such claims are caused by the negligent acts or omissions of Owner.
- C. Notwithstanding any provision of this Agreement and to the extent permitted by law, neither Contractor nor any of its subsidiaries, affiliates, directors, officers, employees, or agents, shall be liable to Owner for any punitive, indirect, incidental, consequential, reliance or special damages or for lost revenues, lost savings or lost profits of any kind, regardless of the form of action.
- D. To the fullest extent permitted by law, Contractor's total cumulative liability to Owner arising out of or relating to this Agreement, whether in contract, tort, or otherwise, shall not exceed the total amount actually paid by Owner to Contractor under this Agreement.



XIV. ACCESS & UTILITIES.

- A. Owner will allow free access to all work areas for workers and vehicles, and will allow areas for storage of materials and debris (dumpster on site (if necessary), provided by Contractor). Driveways will be kept clear for the movement of vehicles during work hours, when made aware of work hours in advance. Contractor will make reasonable efforts to protect driveways, decks, lawns, shrubs, and other vegetation throughout the Project.
- B. Owner shall provide and maintain water and electric service, connect permanent electrical service, gas service or oil service, whichever is applicable, during the entirety of the Project. Owner shall permit Contractor to use, at no cost, any electrical power and water use necessary to carry out and complete the Project.

XV. GOVERNING LAW & DISPUTE RESOLUTION.

- A. This Agreement shall be construed in accordance with and governed by the laws of the State of Maryland. The Parties will cooperate with each other to resolve conflicts informally. If it is not possible, conflicts between the Parties will be resolved by mediation, provided by Community Mediation. If the dispute remains unresolved after mediation, the Parties agree that any claim, dispute, or controversy arising out of or relating to this Agreement shall be resolved exclusively by binding arbitration administered by the American Arbitration Association (AAA). The arbitration shall be conducted in the jurisdiction in which the Job Site is located, and judgment upon the award rendered by the arbitrator may be entered in any court having jurisdiction thereof.

XVI. WARRANTIES.

- A. Contractor warrants that the Services will meet trade standards of good workmanship and warrants the labor for a period of one (1) year from the date of substantial completion. Contractor will make reasonable efforts to blend existing textures, colors, and planes; however, exact duplication is not guaranteed.

Contractor warrants that materials furnished shall be of good quality. Owner's remedy for defects in manufactured materials shall be limited to the applicable manufacturers' warranties.

This warranty applies to labor only and does not cover defects or damage resulting from normal wear and tear, misuse, abuse, neglect, failure to properly maintain the improvements, structural movement or settlement, water intrusion arising from pre-existing conditions, or work performed or modified by others.

XVII. CRITICAL DISCLOSURES.

- A. Owner agrees to the below terms and conditions:

- **Understanding Home Improvement Contract.** Please note, that Contractor tries to make its contracts as detailed as possible and strives to include everything upfront to ensure successful completion of the Project. Our contract is item specific. The only scope of work included is the scope described in Proposal. Contractor shall not be responsible for any interpretation of the scope beyond what is expressly stated in this Agreement and the Proposal. Only items specified in the contract are included. Please read each item in the contract. If it is not expressly noted and described in the scope, it is NOT part of the contract, and NOT included.

Owner's Signature:

R. John King

A1EFF9FF7DCB4C2...

- Contractor utilizes a **pre-determined pricing application (the "Guide")** for proposal preparation and pricing transparency. Only the pricing included in the executed Agreement or an approved change order is binding. Owner acknowledges that during the proposal preparation process, pricing may have been presented for certain optional or alternative items. If such items are not included in the executed Agreement and are later requested after construction has commenced, Contractor may not be able to honor previously presented pricing due to the stage of construction. Any such work shall be subject to revised pricing and must be approved through a written change order prior to commencement.

Signed by:

Owner's Signature:

R. John King

A1EFF9FF7DCB4C2...

- **Contractor shall not be responsible for lawn damage** resulting from normal construction activities related to the Project (for example, reasonable foot traffic required to access the Job Site). Contractor agrees not to drive vehicles or heavy construction equipment on the lawn. Contractor recommends that Owner engage a landscaping contractor to address any lawn restoration following completion of the Project.

Owner's Signature:

R. John King

A1EFF9FF7DCB4C2...



- **Owner shall be responsible for replacing air filters every ten (10) days** for any forced-air heating or cooling equipment with ductwork located within the work area, in order to prevent potential damage to such equipment. Owner accepts responsibility for any damage to HVAC equipment resulting from failure to replace filters in a timely manner.
Signed by: R. John King
Owner's Signature: A1EFF9FF7DCB4C2...
- **All basement work areas must be fully cleared and free of personal property** by the time of the Parties' Pre-Construction Meeting. Owner may store personal belongings in unfinished areas of the basement. Contractor shall not be responsible for the protection of, covering of, or any damage to items remaining in the basement during the Project. Owner's Initials: RJK
- **Any internet, cable, or related service equipment located within the work areas must be relocated** outside of such areas by the time of the Parties' Pre-Construction Meeting. Contractor recommends that Owner contact the applicable service provider to arrange for proper relocation. Contractor shall not be responsible for the protection of, covering of, or any damage to equipment remaining in the basement during the Project. Owner's Initials: RJK
- Upon completion of the Project, **Owner shall be responsible for contacting Owner's cable and/or internet service provider to connect any newly installed low-voltage wiring** to the provider's equipment or service lines. Contractor shall not be responsible for making such connections and is unable to perform this work due to potential risks associated with interfering with the provider's equipment or systems. Owner's Initials: RJK
- **Owner shall be responsible for contacting the security and/or fire alarm service provider** to request removal of any sensors or related equipment located within the finished space or in areas affected by new walls, ceilings, or other structures. Owner shall also be responsible for arranging re-installation of such sensors or equipment after completion of the Project. Owner's Initials: RJK
- Any equipment or personal property, including but not limited to **freezers, refrigerators, gym equipment, dehumidifiers, pool tables, furniture, or similar items**, must be relocated outside of the work areas by the time of the Parties' Pre-Construction Meeting. Contractor shall not be responsible for the protection of, covering of, moving of, or any damage to items remaining in the basement during the Project. Owner's Initials: RJK
- **If Contractor is finishing an existing laundry room** in Owner's basement and Owner has not made any arrangements with Contractor to accommodate the washer and dryer during construction, **Contractor needs to have these items relocated outside of the work areas**. Please note, Contractor is not responsible for protection, covering and/or any damages to the equipment left in the basement during the Project. Owner's Initials: RJK
- **Owner shall be responsible for protecting any personal belongings stored in unfinished areas of the basement**. Contractor shall not be responsible for the protection of, covering of, or any damage to personal property or equipment remaining in the basement during the Project. Owner's Initials: RJK
- For safety purposes, **Contractor requests that Owner minimize presence in the construction areas** while work is being performed. Owner shall ensure that children and unauthorized persons do not enter the work areas during the duration of the Project. Failure to adhere to these safety requirements may result in injury. Owner agrees to strictly comply with these safety provisions. Owner's Initials: RJK
- **Dumpster Use.** The dumpster provided for the Project shall be used exclusively by Contractor and its subcontractors. Disposal of personal items or construction debris by Owner or any non-affiliated third party is strictly prohibited. Any unauthorized use of the dumpster shall result in a charge of Five Hundred Dollars (\$500) per occurrence. Owner's Initials: RJK
- **Delivery of full-size refrigerators into the home or basement is outside the scope of Contractor's Services.** Contractor's employees and subcontractors are prohibited from delivering full-size refrigerators. If Owner intends to install a full-size refrigerator in the basement, Owner shall be responsible for arranging delivery and placement of such item. Owner's Initials: RJK



- **Contractor strongly recommends that all decision-makers be present at the Pre-Construction Meeting**, as important questions may arise and input from all relevant parties may be required to avoid delays or misunderstandings. **Owner's Initials:** RJK

- **If the basement is not properly cleared and the condition of the space cannot be fully inspected during the consultation**, Contractor shall not be held responsible for any unforeseen issues, deficiencies, or additional work requirements that were not visible at the time of the initial estimate. In such cases, the Company reserves the right to issue a change order and **additional charges may apply**. **Owner's Initials:** RJK

B. Base Price Bathroom Disclosures and Prefab Showers and Tubs.

- **Prefab Showers and Tubs.** Contractor offers a variety of prefabricated shower and tub options. All available options are caulkless, maintenance-free, and of comparable quality and price. Models vary in size, configuration, and drain location. **Contractor shall select the appropriate model based on Owner's specific project conditions, including bathroom dimensions and rough-in measurements, as well as product availability.** Owner acknowledges that **not all models are available at all times, and Contractor cannot guarantee availability of any specific model for the Project.** **Owner's Initials:** RJK

C. "Flooring by others" disclosures.

- **Unfinished Basement Staircase Protection.** If staircase finishing (including staining, painting, or carpeting) is not included in the Agreement and an existing staircase is located within the work area, Contractor shall not be responsible for preserving or protecting the unfinished staircase from normal wear and tear during the Project, including incidental paint overspray. Contractor shall, upon completion of the Project, remove drywall compound buildup and sweep and vacuum the staircase. If Owner wishes to have the staircase preserved in its pre-construction condition, Contractor may provide protective services for an additional charge of Four Hundred Fifty Dollars (\$450). **Owner's Initials:** RJK
- **Concrete Slab Preparation.** If flooring installation is not included in the Agreement, floor preparation—including wet mopping, paint removal, scraping, or detailed surface cleaning—shall not be Contractor's responsibility. Contractor shall, upon completion of the Project, remove drywall compound buildup and sweep and vacuum the concrete floor. If Owner wishes to have the concrete slab preserved in its pre-construction condition Contractor may provide such services at a rate of One Dollar and Twenty Cents (\$1.50) per square foot. **Owner's Initials:** RJK
- **Floor Leveling After Plumbing Groundwork.** If flooring installation is not included in the Agreement, floor leveling—including any leveling required following plumbing groundwork—shall not be Contractor's responsibility. Such work is considered part of the floor preparation process to be performed by the flooring contractor. **Owner's Initials:** RJK

D. Demolition disclosures.

- **Asbestos and Lead Paint Disclosure.** Owner shall disclose to Contractor the presence of any known or suspected asbestos-containing materials or lead-based paint at the Job Site prior to commencement of work. While removal of certain lead-based paint components may be performed as part of Contractor's demolition scope, removal, abatement, or remediation **of asbestos-containing materials is not included in the Contract Price unless expressly stated in the Agreement or an approved change order.** **Owner's Initials:** RJK
- **Plaster Demolition Disclosure.** Owner shall inform Contractor of the presence of plaster walls or ceilings at the Job Site prior to commencement of work. Failure to disclose such conditions will result in additional demolition charges, which shall be addressed through a written change order. **Owner's Initials:** RJK



- E. **Sewage pump disclosure.** If the Project includes a sewage ejector pump, grinder pump, or similar system, Owner acknowledges that improper use may result in clogging, pump failure, or motor burnout.

Owner shall ensure that only wastewater and standard toilet paper are introduced into the sewage system. The following items shall never be flushed or discharged into the sewage pump system, as they may cause clogging or damage:

- **Disposable wipes, such as baby wipes or personal hygiene wipes, even products described as "biodegradable" or "OK for use in septic systems" may NOT be OK: if your system uses a septic pump or grinder pump or sewage ejector pump as this material can clog the pump impeller and cause expensive pump damage or motor burnout.**
- *Cigarette butts are not biodegradable and should not be flushed into the sewage pump receptor. In addition, the filters on cigarette butts can clog and destroy sewage pump.*
- **Clothes dryer sheets** used as fabric softener or to make your dry clothes "smell nicer." The synthetic fabric from which dryer sheets are made will not break down in the sewage pump tank and will clog the pump.
- **Cotton swabs (Q-tips®)** have been known to clog a drain or two as they are not biodegradable, though trivial in volume. If your system uses a septic pump or grinder pump or sewage ejector pump, this material can clog the pump impeller and cause expensive pump damage or motor burnout.
- **Dental floss** is not biodegradable, though trivial in volume.
- **Diapers and similar items**, which are not biodegradable, will simply clog a septic system and are very likely to clog building drains.
- **Latex products:** gloves or similar products.
- **Paper towels** and facial tissues (Kleenex™) do not break down easily and should not be flushed into the septic system. Toilet paper breaks down quickly and should not be a problem in an ordinary septic tank system.
- **Panty liners** should never be flushed down a building drain.
- **Plastic bags** or other plastic scrap or trash of any kind should never be flushed down a building drain.
- **Sanitary napkins** should never be flushed down a building drain.
- **Tampons** should not be flushed down a building drain.
- **Any other solid, semi-solid objects** that do not dissolve readily in water.

If flushing any of the above-listed items results in damage to the sewage pump, any applicable sewage pump warranty shall be deemed void due to misuse. In such event, Owner shall be responsible for a sewage pump replacement fee of One Thousand Dollars (\$1,000) and/or a cleaning fee of Five Hundred Dollars (\$500), as applicable.

All applicable fees must be paid in full prior to any repair, replacement, or service being performed.
 Owner's Initials: Initial KJK

XVIII. DESIGN SERVICES

- A. **Design Services.** Contractor agrees to provide interior design services to Owner as specified in the Proposal. The amount of Interior Designer time included for each applicable item shall be limited to the number of hours stated in Proposal. Included design time encompasses all services related to the design process, including but not limited to in-person or virtual consultations, phone calls, email communications, preparation of schematics or drawings, material selections, and coordination with vendors or suppliers.
 Any design services exceeding the allocated hours set forth in the Project scope shall be subject to additional charges.
 Owner's Initials: Initial KJK
- B. **Additional Design Services.** Once the design time included has been exhausted, Contractor agrees to provide additional design services at a concessionary rate of Sixty-Seven Dollars and Fifty Cents (\$67.50) per hour.
 Owner's Initials: Initial KJK
- C. **Hours of Operation.** Contractor's standard hours of operation are Monday through Friday, between 9:00 a.m. and 5:00 p.m. Any design consultations requested outside of these hours shall incur a fee of Two Hundred Dollars (\$200), payable in full prior to the scheduled appointment. One hundred percent (100%) of this fee is paid directly to the Interior Designer. Owner's Initials: Initial KJK



XIX. WIFI ACCESS.

Owner shall provide Contractor with reasonable access to a Wi-Fi network at the Job Site, as Contractor utilizes cloud-based project management tools that require internet access. Such tools are used for photo and video documentation, communication, and reporting, which are important for the successful and timely completion of the Project.

Owner may provide access to the primary Wi-Fi network or create a separate guest network for Contractor's use. Information regarding the creation of a guest Wi-Fi network can be provided upon request. **Owner's Initials:** RJR

XX. SIGNATURES.

Owner is entitled to a filled in copy of this Agreement, signed by both Owner and Contractor before any work may be started. Owner may cancel this transaction at any time prior to midnight of the third (3rd) business day after the date of this Agreement. See the Notice of Cancellation form for an explanation of this right.

This Agreement is entered into as of the date written below.

Owner(s) printed name(s): R. John Ring

Owner(s) Signature(s): R. John Ring
Signed by: A1EFF9FF7DCB4C2...

~~Date~~ 11/20/2020

Contractor's Printed Name: Pavel A. Abaev

Contractor's Signature Pavel A. Abaev

~~Date~~ 11/20/2020



NOTICE OF RIGHT TO CANCEL

3/31/2026

Date of transaction

OWNER MAY CANCEL THIS CONTRACT, WITHOUT ANY PENALTY OR OBLIGATION, WITHIN THREE (3) BUSINESS DAYS FROM THE ABOVE DATE.

If Owner cancels, any property traded in, any payments made by Owner under the contract or sale, and any negotiable instrument executed by Owner will be returned within ten (10) business days following receipt by Contractor of Owner's cancellation notice, and any security interest arising out of the transaction will be canceled.

If Owner cancels, Owner must make available to Contractor at Owner's residence, in substantially as good condition as when received, any goods delivered to Owner under this contract or sale. Owner may, if they wish, comply with the instructions of Contractor regarding the return shipment of the goods at Contractor's expense and risk.

If Owner makes the goods available to Contractor and Contractor does not pick them up within twenty (20) days of the date of Owner's Notice of Cancellation, Owner may retain or dispose of the goods without further obligation. If Owner fails to make the goods available to Contractor, or if Owner agrees to return the goods and fail to do so, Owner remains liable for performance of all obligations under the contract.

To cancel this transaction, mail or deliver a signed and dated copy of this Cancellation Notice, to:

ACH GROUP LLC DBA BASEMENTREMODELING.COM at 5300 Kilmer pl, Hyattsville, MD, 20781

NOT LATER THAN MIDNIGHT OF 4/3/2026.

Date

I HEREBY CANCEL THIS TRANSACTION.

Date

Owner's Signature

ACKNOWLEDGEMENT OF RECEIPT

Each of the undersigned acknowledges receipt of two (2) copies of this Notice of Right to Cancel.

Signed by:

R. John King

Owner's Signature

3/31/2026

Date

Owner's Signature

Date





PROPOSAL

Owner Name: John Ring
Address: 5801 Searl Ter, Bethesda, MD, 20816
Phone Number: (603)-996-1707
Email Address: rayjohnring@gmail.com
Date: 03/27/2026

**Highest-Rated Basement Finishing
and Remodeling Company**
in Maryland, Virginia and Washington, DC

*with 500+ reviews on
Angieslist.com, Houzz.com, Google.com, etc.*

Ask about our waterproofing services

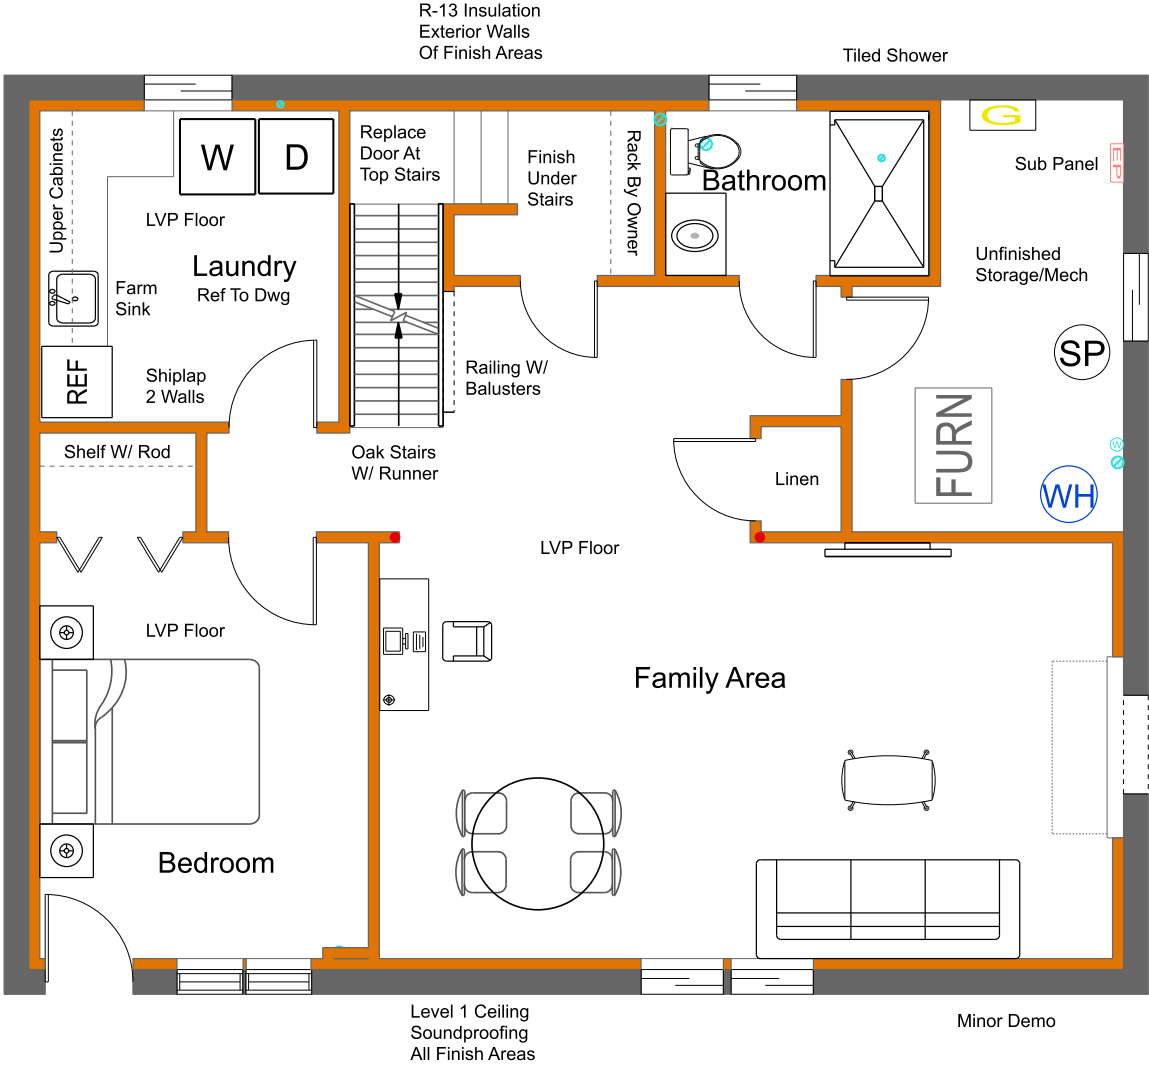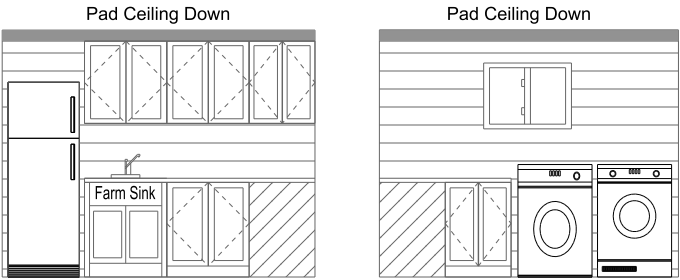


ATTACHMENT 1: FULL PROJECT SCOPE.**BASEMENT TOTAL SQ. FT. = 754 SQ. FT.****ATTENTION! PROPERTY ON SEPTIC? BEDROOMS OR ROOMS WITH CLOSETS ARE NOT POSSIBLE UNLESS WRITTEN CONFIRMATION FROM COUNTY/CITY HEALTH DEPARTMENT IS PROVIDED! THIS INCLUDES REMODELING PROJECTS WITH EXISTING ROOMS!**

1. Basement Base Price	\$59,227		
1-3. Prince George's and Montgomery Counties	Quantity	Price	Zone Adjusted Total
ITEM 1-3-2. Montgomery County Permits and Inspections DISCLOSURES: - Permits and inspections item does not include any hoa related tasks. Please refer to items 1-1-5. HOA help. Contractor will submit specs and all necessary forms to HOA and 1-1-4. HOA help. Contractor will submit specs to Homeowner only - In case permits office requests a plot plan—which occurs in about 5% of cases depending on property details and scope items such as egress windows and walk-outs—the client is responsible for providing a plot plan stamped by a licensed surveyor. If the client does not already have a stamped plot plan in the surveyor package received when the house was purchased, the client may either hire a licensed surveyor directly or have BasementRemodeling.com obtain the plot plan at an average cost of \$400-\$800.	1	N/A	N/A
ITEM 1-3-3. Property on Public sewer. Health department approval is not required.	1	N/A	N/A
1-6. Demolition	Quantity	Price	Zone Adjusted Total
ITEM 1-6-1. Minor demolition. Under 2 hours Includes light demolition tasks such as removal of small non-structural items like wall trim, baseboards, cabinetry, a few wall panels, or isolated drywall sections. Does not include full room or full bathroom demolition, electrical removal, plumbing demo, etc.	1	N/A	N/A
Custom item: ELECTRICAL DEMO CLEAN UP	1	Custom	\$900
1-7. House Specifications	Quantity	Price	Zone Adjusted Total
ITEM 1-7-1. Ceiling height 8 feet or less	754	N/A	N/A

ITEM 1-7-3. Direct access to the basement from the outside	1	N/A	N/A
1-9. Basement Base Price	Quantity	Price	Zone Adjusted Total
ITEM 1-9-1. Basement Base Price	754	N/A	N/A
ITEM 1-9-2. Framing and Fire blocking. All basement walls and bulkheads per Owner's request and provided sketches. (2x4 lumber studs with treated sill plates, 16 inches on center). Ceiling bulk heads framed per existing site conditions (framing around all existing plumbing, mechanical and electrical utilities ran below floor joists). Base price may include one space (room) and one finished closet space per 500 sq. ft. of finished area. SHELVING IS NOT INCLUDED WITH THE CLOSETS, SINCE EACH OF OUR CLIENTS HAS DIFFERENT PREFERENCES ON THE SHELVING. REFER TO ITEMS 3-13-1. Add closet single wire shelf (up to 6 ft.) THROUGH 3-13-5. Add wire shelving ClosetMaid system into the closet: 7-ft. - 10-ft. OWNER INITIALS: 	N/A	N/A	N/A
ITEM 1-9-3. Drywall. 1/2" regular drywall - all walls and ceiling. Level 4 Finish. Level 4 is the Used by every non-custom home builder in the country. Used by 90% of custom home builders in the country. Joints are to follow a three-coat system, consisting of; (1) a tape coat plus (2) two subsequent coats applied over the tape coat and fastener heads. All joint compounds should be sanded to a smooth finish free of tool marks and ridges. Drywall surface itself is not skim-coated. Level 4 with Satin Paint:  You may see joint lines, uneven textures, or minor flaws in lighting-sensitive areas. OWNER INITIALS: 	N/A	N/A	N/A
ITEM 1-9-4. Electrical Rough-in and Finish. All electrical work to be performed in accordance with state and local codes. • IC-Rated 6" Recessed Lights or Flushmount LED lights for bulkheads/closets etc - location per Owner's request. QTY: 16 • For additional light refer to item 2-8-1 - \$240/light • LED light bulbs 2700k • Cable/low voltage - location per Owner's request. QTY: 1 • Toggle (not Decora) switches/outlets per code (3- and 4-way where required) • Basic plastic or steel toggle (not Decora) switch/outlet plates (white, almond or ivory). PAINTING THE PLATES NOT INCLUDED. • Basement smoke and Combo (smoke + CO) detectors will be installed per code. • Mechanical/unfinished area lighting is included: ◦ Areas under 16 sq. ft. (4'x4') - pull light only (lamp holder with pull) (add switch 20\$) ◦ Areas over 16 sq. ft. - Switch and one utility light (lamp holder) per 100 sq. ft. (Additional. Light - 20\$) After Project completion Owner will need to contact Owner's cable/internet service provider to connect newly installed low voltage lines to Owner's provider's equipment/lines. Due to some implications that may be caused by interfering with Owner's provider's equipment, Contractor is unable to perform this connection.	N/A	N/A	N/A

ITEM 1-9-5. Add Ductwork. One air register per 250 sq. ft. or less. Basic white air register and return vents only included. Painting vents is extra cost. 1 Air return for the basement.	N/A	N/A	N/A
ITEM 1-9-6. Finish Carpentry - General specs Initial RJR • ANY DOORS UNDER 80" WILL BE BILLED AT THE RATE OF \$200 PER DOOR. OWNER INITIALS: _____ • STANDARD Doors (See doors page below for included styles), UNLESS STATED OTHERWISE. QTY: 4 • STANDARD 2 ¼ Door/Window trim - WM-327, WM-472 and WM-371 PROFILE ONLY, UNLESS STATED OTHERWISE. Does not include rosettes (additonal corner piece) or plinth block (additonal piece at the base of the door casing). • STANDARD 3 ¼ Baseboard - WM-623, WM-432 or WM-663 PROFILES ONLY, UNLESS STATED OTHERWISE. • Basic pine stair rail (banister) painted white semi-gloss WM-240 PROFILE ONLY, UNLESS STATED OTHERWISE • Wrap all basement columns with one-piece chair rail WM-300 PROFILE ONLY and one-piece crown molding WM-49 PROFILE ONLY, UNLESS STATED OTHERWISE • \$30 door lock allowance per each door included PLEASE NOTE, IT IS OWNER'S RESPONSIBILITY TO UNDERSTAND WHAT DOOR AND TRIM PROFILES ARE INCLUDED. PLEASE "GOOGLE" PROFILE NAMES FOR MORE INFORMATION. Initial RJR OWNER INITIALS: _____	N/A	N/A	N/A
ITEM 1-9-7. 8lb Padding and Carpet. Can be exchanged for Painted floor or steps.	N/A	N/A	N/A

ITEM 1-9-8. Painting details - General Specs GENERAL SPECS: - Filling and caulking all nail-holes and gaps. - One coat of Contractor's grade primer on all walls and ceiling - Sherwin Williams 200. WHITE ceiling paint and FLAT COLORED paint on the walls PAINT FINISH UPGRADE TO SATIN/EGGSHELL WILL RESULT IN EXTRA COST OF \$4/SQ. FT. due to the following reasons: 1. Level 5 drywall finishing required; 2. High sheen finishes cost more per gallon; 3. Touching up high sheen finishes will require painting the entire wall; 4. Flat paint evens out imperfections that might show with high sheen finishes, particularly the drywall joints. This results a lot in additional work; 5. Working with high sheen finishes requires more expertise and experience overall. - White Sherwin Williams 200 SEMI-GLOSS paint for doors and trims CONTINGENCIES: All ceilings to be white (colored ceiling - extra cost) Deep dark colors (more than 2 coats of paint are necessary) will result in extra cost Accent wall - extra cost Custom painting will result in extra cost 1 COLOR PER ROOM. MORE THAN ONE COLOR PER ROOM WILL RESULT IN EXTRA COST PAINTING OF EXISTING WOOD WINDOWS IS NOT INCLUDED. PLEASE REFER TO ITEM 1-12-3 - PAINTING OF EXISTING WOOD WINDOWS IS NOT INCLUDED. PLEASE REFER TO ITEM 1-12-4 OWNER INITIALS: <u>Initial RJR</u>	N/A	N/A	N/A
ITEM 1-9-9. Interior designer help - 4 hours - GENERAL SPECS - BASEMENT LAYOUT HELP - FLOORING AND PAINT SELECTION TOTAL OF FOUR (4) HOURS INCLUDED EXCLUDES PRE-CONSTRUCTION MEETING WHICH IS NOT BILLED OWNER INITIALS: <u>Initial RJR</u>	N/A	N/A	N/A
ITEM 1-9-10. Consultation fees for design services conducted outside of regular working hours. Our business operates Monday through Friday, between 9 am and 5 pm. Design consultations requested and conducted outside of normal business hours will result in a fee of \$200, payable before the scheduled appointment. 100% of the fee goes directly to the interior designer. OWNER INITIALS: <u>Initial RJR</u>	N/A	N/A	N/A

ITEM 1-9-11. No credits for base price items Please acknowledge that no credits will be issued for unused base price items.. By signing the contract, you accept these terms. OWNER INITIALS: 	N/A	N/A	N/A
Custom item: CREDIT FOR PRICE MATCHING PREVIOUS PROPOSAL COSTS	1	Custom	\$-2,168
1-11. Framing, Drywall and Paint	Quantity	Price	Zone Adjusted Total
ITEM 1-11-3. Additional room	1	N/A	N/A
1-12. Baseboards and Trims	Quantity	Price	Zone Adjusted Total
ITEM 1-12-1. Upgrade Baseboard to 5 ½", 1x4, or 1x6. STANDARD SINGLE MEMBER ONLY baseboard up to 5 ½", 1x4, or 1x6, unless otherwise specified. Does not include custom-milled profiles.	1	N/A	N/A
ITEM 1-12-3. Upgrade Door/window casing to 3 ½", 1x3, or 1x4. STANDARD SINGLE MEMBER ONLY door/window casing up. Does not include custom-milled profiles. Does not include rosettes (additonal corner piece) or plinth block (additonal piece at the base of the door casing).	1	N/A	N/A
1-13. Interior Doors	Quantity	Price	Zone Adjusted Total
ITEM 1-13-3. Additional regular hollow core door	2	N/A	N/A
ITEM 1-13-4. Upgrade to double Bi-fold door	1	N/A	N/A

2. Insulation and MEP Code Requirements		\$3,390	
2-1. Electrical	Quantity	Price	Zone Adjusted Total
ITEM 2-1-1. Subpanel Install within 5 feet of the main electrical panel.	1	\$995	\$935
ITEM 2-1-7. Dedicated line for fridge/freezer/sump pump in the basement.	1	\$350/ each	\$329
2-3. Insulation	Quantity	Price	Zone Adjusted Total
ITEM 2-3-1. R-13/15 fiberglass Insulation. VIRGINIA OR MARYLAND ONLY!	754	N/A	N/A
3. Basement upgrades		\$18,402	
3-7. Soundproofing	Quantity	Price	Zone Adjusted Total
ITEM 3-7-1. Ceiling soundproofing LEVEL 1 - R-30 Fiberglass. PLEASE NOTE: That there are no industry standards or building code requirements for soundproofing in residential construction. The soundproofing levels used by BasementRemodeling.com are proprietary and unique to our company. If you find similar terms or level descriptions elsewhere online, please note that they do not reflect the same materials, techniques, or performance expectations defined by BasementRemodeling.com. We do not guarantee any equivalency between our proprietary system and classifications used by other vendors and installers.	754	\$3.5/sq. ft. \$575 minimum	\$2,481
3-9. Electrical and low voltage	Quantity	Price	Zone Adjusted Total
ITEM 3-9-8. Basic Dimmers.	4	\$55	\$207
3-13. Shelving	Quantity	Price	Zone Adjusted Total
ITEM 3-13-2. Add closet single melamine shelf with hanging rod (up to 6-ft.)	1	\$320	\$301

3-15. Wall and ceiling designs	Quantity	Price	Zone Adjusted Total
ITEM 3-15-8. Ship lap paneling 1/2 in. x 5-1/4 in., painted. Walls and ceilings. Design, product specification and drawings by Interior designer required. Please refer to Interior Design Clause.	152	\$11.50/sq. ft. \$1,400 minimum	\$1,643
3-17. Railings and Stairs	Quantity	Price	Zone Adjusted Total
ITEM 3-17-4. One-piece, solid red oak, stained handrail.	2	\$495	\$931
ITEM 3-17-8. Upgrade existing staircase with stained red oak stair treads and painted/stained risers. Does not include overhanging steps or exposed "cut" stringer (stairs skirting or skirtboard). Does not include landing(s) - refer to item 3-17-9. Landing for red oak stair treads	11	\$315/step	\$3,257
ITEM 3-17-9. Landing for red oak stair treads	1	\$735/landing	\$691
ITEM 3-17-13. Railing with wood spindles. Stained or painted. 6210 PROFILE RED OAK ONLY! Refer to railing brochure for included spindles and post styles. May require handrail to match - refer to ITEM 2-15-4 and ITEM 2-15-5. Design, product specification and drawings by Interior designer required. Please refer to Interior Design Clause.	1	\$1,575/ side	\$1,481
Custom item: CARPET RUNNER	1	Custom	\$1,200
3-18. Flooring	Quantity	Price	Zone Adjusted Total

ITEM 3-18-2. LVT/LVP Installation (Upgrade from base price carpet). Includes Installation, shoe molding and all materials. LVT Brands: Durato Panzu, Durato Azul Tortuga, Allegheny, Shenandoah, Rock Lock Plus II, Rock Lock Plus Tile, Superior Lock Plus, Coretec Pro, and Harborview. LVT INSTALLATION ON THE PAINTED FLOOR WILL VOID ANY MANUFACTURER'S WARRANTY. Floor leveling is not included. NO PATCH INSTALLATIONS (ENTRY, BAR AREA) WHERE MORE THAN ONE TRANSITION REQUIRED. 2 hours of Interior designer time is included.	734	\$6/sq. ft. \$1,200 minimum	\$4,140
ITEM 3-18-9. Floor leveling. All included. Under certain circumstances, the contractor may agree to credit the "floor leveling" item and not perform any subfloor leveling prior to installation. In such cases, the customer acknowledges and agrees to the following: • Warranty Impact: Skipping floor leveling will likely void the flooring manufacturer's warranty. • Structural Concerns: The floor may feel soft, hollow, or uneven underfoot due to the underlying concrete slab irregularities. • Separation & Gaps: The flooring may begin to separate at the seams or develop visible gaps over time. • Movement & Shifting: Uneven subfloors can cause the floating floor to shift, creak, or move under pressure. • Excessive Wear: Stress points caused by uneven support may cause damage to the locking mechanisms between planks. • Moisture Trapping: Low spots in the slab or subfloor may collect moisture, leading to swelling, warping, or mold/mildew issues beneath the flooring. • esthetic Defects: Visible height differences, lippage, or "bounce" may occur, negatively affecting the look and feel of the finished floor. By accepting a credit in place of floor leveling, the customer understands these risks and releases the contractor from responsibility for any problems that arise from the installation of flooring over an unlevel surface. OWNER INITIALS: <u>RJR</u>	734	\$3/sq. ft.	\$2,070
4. Base price bathroom	\$11,844		
4-2. Base price for full/half bathroom	Quantity	Price	Zone Adjusted Total
ITEM 4-2-1. Base Price Full Bathroom	1	\$12,600	\$11,844
ITEM 4-2-3. Underground plumbing within 5 ft. from 3" or 4" stack or existing toilet Underground plumbing within 5 ft. from 3" or 4" stack or existing toilet is included if necessary. Back water valve is included ONLY IF REQUIRED BY CODE.	N/A	N/A	N/A

ITEM 4-2-4. Hot/cold water supply lines and above ground drain lines and venting Hot/cold water supply lines and above ground drain lines and venting.	N/A	N/A	N/A
ITEM 4-2-5. Framing bathroom walls with 2x4 wood studs.	N/A	N/A	N/A
ITEM 4-2-6. Electrical (rough-in): Dedicated 20Amp circuit for bathroom GFCI outlet	N/A	N/A	N/A
ITEM 4-2-7. Vanity light: Vanity light installation	N/A	N/A	N/A
ITEM 4-2-8. Overhead shower/tub light: Overhead shower/tub light installation.	N/A	N/A	N/A
ITEM 4-2-9. AC / heating outlet (cut-ins into existing air duct)	N/A	N/A	N/A
ITEM 4-2-10. Exhaust fan installation and venting to outside	N/A	N/A	N/A
ITEM 4-2-11. Drywall. Green board (Mold-resistant drywall) in the entire bathroom.	N/A	N/A	N/A
ITEM 4-2-12. Sterling by KOHLER Caulkless Tub or Shower System. Unless specified otherwise. (Accord, Ensemble). Availability of different models and sizes varies and not guaranteed. Seat is not included. Refer to Showers and Tubs pages for details.	N/A	N/A	N/A
ITEM 4-2-13. Flooring. 12x12 or larger tile on the floor. Straight or staggered design only (sealing the grout is not included)	N/A	N/A	N/A
ITEM 4-2-14. Finished carpentry. Baseboards and trims installation.	N/A	N/A	N/A
ITEM 4-2-15. Single Vanity, Vanity top, vanity faucet, vanity light installation, and hook-up. DOES NOT INCLUDE IKEA VANITIES, WALL MOUNT VANITIES, DOUBLE VANITIES. Refer to vanity upgrades section for upgrades	N/A	N/A	N/A
ITEM 4-2-16. Toilet installation and hook-up.	N/A	N/A	N/A

ITEM 4-2-17. Storage cabinet/mirror installation per customer's request.	N/A	N/A	N/A
ITEM 4-2-18. Other Bathroom Hardware. Shower Curtain rod/towel rack/toilet paper holder etc. installation per customer's request	N/A	N/A	N/A
ITEM 4-2-19. Painting. Semi-gloss WHITE paint for ceiling and doors/trim. Eggshell Contractor's grade COLOR paint on the walls.	N/A	N/A	N/A
ITEM 4-2-20. ALL FULL BATHROOM DECORATIVE ITEMS ARE TO BE PURCHASED BY OWNER. All bathroom decorative items to be purchased/paid for by owner. Contractor will pick up/deliver any bulky and heavy items. What is not included: • Shower faucet • Exhaust fan • Tile flooring • Vanity and top • Vanity faucet • Vanity light • Vanity mirror • Toilet • Bathroom hardware Initial RJR OWNER INITIALS: _____	N/A	N/A	N/A

5. Bathroom upgrades		\$6,439		
5-3. Shower upgrades		Quantity	Price	Zone Adjusted Total
ITEM 5-3-4. Tiled shower surround. Basic design with corner shelf and corner seat (not tiled) W/ TILED SHOWER PAN. Please note the following: • Tile materials are not included. • In-shower window will result in an upcharge! Refer to 5-3-10. Upcharge for in-shower window niche tile work. • Straight or staggered tile layout only (grout sealing is not included). • Full-wall mosaic tile is not included. • Mosaic accents are included, up to 15% of the wall area. • Recessed shelves (niches) and grab bars are not included. • Please refer tiled surround upgrade items below. 3 hours of Interior designer time is included.		1	\$4,600/ up to walls 90 sq. ft. walls up to 16 sq. ft. shower pan	\$4,324
5-5. Shower/Bathtub doors		Quantity	Price	Zone Adjusted Total
ITEM 5-5-2. Sliding FRAMELESS bathtub/shower doors installation (with rollers on top). Labor only. DISCLOSURE: IT IS OWNER'S RESPONSIBILITY TO ENSURE THAT SHOWER DOORS ARE ON SITE OR READY FOR PICK UP FROM LOCAL HARDWARE STORE WHEN ALL OTHER TASKS ON THE PROJECT ARE COMPLETED. IN CASE OF DELAY, THE COST OF INSTALLATION WILL BE REFUNDED, AND THE INSTALLATION WILL BE CANCELLED.		1	\$800	\$752
5-6. General		Quantity	Price	Zone Adjusted Total
ITEM 5-6-7. Bathroom linen closet with door and with wire shelves.		1	\$1,450	\$1,363
6. Laundry		\$16,369		
6-1. Laundry room price		Quantity	Price	Zone Adjusted Total

ITEM 6-1-3. New laundry with washer and electric dryer. Within 20-ft from drain. Drain, hot/cold water supply lines with washer box. Washer outlet. Dryer outlet and venting. No shelving, cabinets or countertops are included with this item. Please note, washer and dryer connection is complimentary if appliances are on site before the completion of the project. If additional trip will be required to connect washer and dryer \$300 fee will be added. Appliances are not included. OWNER INITIALS: Initial RJR	1	\$4,212	\$3,959
6-2. Laundry room cabinets and countertops upgrades.	Quantity	Price	Zone Adjusted Total
ITEM 6-2-1. Plumbing and electrical rough-in for laundry cabinets and countertop UPCHARGE. Plumbing and electrical rough-in for laundry cabinets and countertop UPCHARGE.	1	\$1,940 + \$22/ln. ft. of piping	\$1,844
ITEM 6-2-3. Sink and Faucet hook-up after counter-top installation. Sink and Faucet hook-up after counter-top installation. Farm sink not included. 6-2-7. Farm sink installation upcharge.	1	\$398	\$374
ITEM 6-2-4. Wall/Base Cabinets installations with knobs, spacers (fillers), tow kick and other supporting cabinet hardware. Wall/Base Cabinets installations with knobs, spacers (fillers), tow kick and other supporting cabinet hardware. 2.5 hours of Interior designer time is included.	14	\$205/ln ft	\$2,698
ITEM 6-2-7. Farm sink installation upcharge. Farm sink installation upcharge.	1	\$430	\$404
6-3. Cabinet and countertop w/sink allowance	Quantity	Price	Zone Adjusted Total
ITEM 6-3-1. Wall/Base Cabinets allowance for A and B series cabinets. Wall/Base Cabinets allowance for A and B series cabinets. KNOBS AND PULLS TO BE PROVIDED BY HOMEOWNER	14	\$300/ln. ft.	\$4,200
ITEM 6-3-7. Quartz countertop allowance. Up to 26" depth (along the wall cabinets or 26" deep island)	9	\$210/ln. ft. + \$300 if < 15 ln.ft	\$2,190

ITEM 6-3-11. Sink and sink cut-out Farm sink is not included! Please refer to 6-2-7. Farm sink installation upcharge.	1	\$700	\$700
---	---	-------	-------



Cost Summary

ACH Group, LLC d/b/a BasementRemodeling.com
MD Lic.: 129172
DC Lic: 410516000631
VA Lic: 2705159425
Address: 5300 Kilmer pl, Hyattsville, MD, 20781
Phone: (877) 224-2434
Fax: (877) 224-3661

Total project cost: \$115,671

Incentive if project started by 05/28/2026: -\$13,378

Final project cost with all applicable discounts: \$102,293

If a credit will be requested for an item in this Proposal after contract is signed, then a credit will be given at the rate proportional to the incentive above.

Payment Schedule

1. **\$1,000** deposit
2. **10%** of the final cost due when contract is signed
3. **15%** of the final cost due when your project starts
4. **25%** of the final cost due when framing, rough-in plumbing, electrical, mechanical is completed (the project is 35% complete)
5. **25%** of the final cost due when the project is 70% complete
6. The rest, **25% of the final cost minus \$1,000**, is due when the project is 100% finished and you are completely happy with the result.



Supporting Documents



BASEMENT
REMODELING.COM
— ALL ABOUT BASEMENTS —

Doors selection

Passage Designs

Smooth Surface – Flat Panel



☐ Craftsman III[™]
Smooth
Craftsman Sticking



☐ Madison[®]
Smooth
Craftsman Sticking



☐ Conmore[®]
Smooth
Stepped Sticking



☐ Monroe Smooth
All Panel
Cove & Bead Sticking



☐ Birkdale[™]
All Panel
Cove & Bead Sticking



☐ Beveled
Mirror
*Other Side: Six-panel
textured only*



Smooth Surface – Raised Panel



☐ Colonial[™]
Textured
Ovolo Sticking




☐ Camden[®]
Textured
Cove & Bead Sticking



☐ Colonist[®]
Smooth
Cove & Bead Sticking



☐ Rockport[®]
Smooth
Cove & Bead Sticking




☐ Princeton[™]
Smooth
Cove & Bead Sticking

Discontinued
by manufacturer



☐ Santa Fe[™]
Smooth
Ovolo Sticking



☐ Cambridge[™]
Smooth
Ovolo Sticking

Discontinued
by manufacturer



Solid pine doors



☐ Carrara[®]
Smooth
Cove & Bead Sticking



☐ Caiman[®]
Smooth
Cove & Bead Sticking



☐ Continental[™]
Smooth
Ovolo Sticking



☐ 044
Four Panel
Raised



☐ 066
Six Panel
Raised



☐ 1011
Single Panel
Shaker



☐ 1022
Two Panel
Shaker



☐ 0732
Plantation Style
Louver



● Hollow core – included
● Solid core – \$200/extra per door

● Painted Solid Pine - \$900 (including Louver door)
● Stained Solid Pine - \$1100 (excluding Louver door)
● Stained Solid Pine Louver door- \$1,500

RAILING WITH BALUSTER

LEGEND



- INCLUDED BALUSTERS AND POST NEWELS PER CONTRACT (STAINED OR PAINTED PER CONTRACT)



- BALUSTERS UPGRADE - \$350 PER SIDE (STAINED OR PAINTED PER CONTRACT)



- OVER THE POST NEWEL - \$250 PER POST UPGRADE



- UPGRADED POST NEWELS AND BOX NEWELS - \$125 PER POST UPGRADE

Wood Quick Reference

Balusters

1-1/4"
Pin Top Balusters



5200 Pg. 42/43
5015 Pg. 50-53
F-5015 Pg. 51/53
5016 Pg. 50/52

1-1/4"
Square Top Balusters



5060 Pg. 46/47
F-5060 Pg. 47
C-5060 Pg. 47
5067 Pg. 50-53
5141 Pg. 50-53
F-5141 Pg. 51/53

1-3/4"
Pin Top Balusters



2015 Pg. 38/39
F-2015 Pg. 39
T-2015 Pg. 39
8-2015 Pg. 39
5300 Pg. 42/43
8-5300 Pg. 53

1-3/4"
Square Top Balusters



2005 Pg. 38/39
F-2005 Pg. 39
T-2005 Pg. 39
8-2005 Pg. 39
5005 Pg. 42/43
8-5005 Pg. 43
5360 Pg. 46/47
F-5360 Pg. 47
C-5360 Pg. 47

Over the Post Newels



3010 Pg. 38/39



F-3010 Pg. 39



T-3010 Pg. 39



8-3010 Pg. 39



4270 Pg. 42/43



8-4270 Pg. 43



4010 Pg. 52/53



F-4010 Pg. 53



4013 Pg. 52/53



F-4013 Pg. 53

Wood Quick Reference

Post to Post Newels



Box Newels

